

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 30, 2009

#### ORR ELEMENTARY SCHOOL

##### DENSON

All building slabs are complete


Structural Steel erection started on June 23<sup>rd</sup> in Area A

Installation of decking on 2<sup>nd</sup> floor is underway

First 2<sup>nd</sup> floor slab pour is scheduled for the week of 7-27-09


The next month's progress will be the completion of all 2<sup>nd</sup> floor concrete slabs, continuation of steel erection, installation of roof deck, start framing exterior walls, begin installation of fire sprinklers, ductwork, cable trays and electrical and plumbing rough-in in the interior of the building.

A. W. ORR



FIRST FLOOR

NORTH KEY PLAN



SECOND FLOOR

NORTH KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 30, 2009

#### CLARKSTON ELEMENTARY SCHOOL

##### RPR

Roofing installation at Area A has started

Brick work has started in Court Yard area.


Ductwork and all above ceiling work is underway in Area A

Framing for interior and exterior walls is started


Structural steel erection is nearing completion with only the Gym, Area D, remaining

Progress for the next month will be the completion of structural steel erection, continuation of wall framing, roofing, masonry along with mechanical, electrical, plumbing and technology rough-in

CLARKSTON



 NORTH KEY PLAN



 NORTH SECOND FLOOR KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 30, 2009

#### WOODS ELEMENTARY SCHOOL

##### DENSON


Structural steel erection started on 6-22-09

Final building slab pour is scheduled for the week of 7-27-09


Foundations and underground Electrical and Plumbing are complete in all areas

The next month's progress will be the start of 2nd floor concrete slabs, continuation of steel erection, installation of roof deck, start framing exterior walls, begin installation of fire sprinklers, ductwork, cable trays and electrical and plumbing rough-in in the interior of the building.

ANDY WOODS



← NORTH  
FIRST FLOOR  
KEY PLAN



← NORTH  
SECOND FLOOR  
KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 30, 2009

#### JONES/BOSHEARS SCHOOL

##### DENSON

Building slabs for Areas E, F, C, D, A & Arena are complete.



Parking lot for Administrative area has been poured

First 2<sup>nd</sup> floor slab pour on Jones is scheduled for week of 7-27.

Steel erection for Areas E & F is complete and erection for Area C is started.

Metal building for Arena has been delivered to site, erection to start next week.

Progress for the next month will be the completion of steel erection in Areas C & D, Start of steel erection in Areas A & B, completion of 2<sup>nd</sup> floor slabs in Areas E & F, Start concrete placement at loop road, start exterior wall framing, start interior ductwork, cable trays, fire sprinklers, electrical and plumbing rough-in

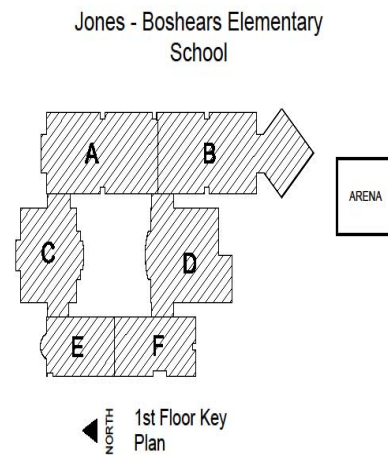

## **2008 BOND**

### **CONSTRUCTION PROGRESS REPORTS**

**July 30, 2009**

#### **GRIFFIN ELEMENTARY**

##### **DENSON**

**Bids for the new Athletic Field on the site of the Boys & Girls Club and the creation of a play field on the Dogan campus have been received and presented to the Board for approval.**

**Design for the new school is 65% complete which is 10% ahead of schedule. 95% review documents are expected on 8-15-09.**
